

Project Plan

DriveTree

Team Member	Heemal Syangbo
Team Member	Anudhin Thomas
Team Member	Jeffin Yohannan
Team Member	Nasharudhin Feroz

Document Revision History

Revision #	Date
1.0	October 6, 2025

Table of Contents

Section	Title	Page
1	Executive Summary	3
2	Project Approvers, Reviews and Distribution List	3
3	Scope	4
4	Deliverables	4
5	Assumptions	5
6	Dependencies	5
7	Risk Management	5
8	Communication	6
9	Task Listing (WBS – Work Breakdown Structure)	6
10	Gantt Chart	7
11	Milestones	7
12	RAM – Responsibility Assignment Matrix	8
13	Approval	8

1. Executive Summary

The following describes the project to be executed.

DriveTree is a digital marketplace connecting licensed driving instructors with students seeking lessons. It simplifies scheduling, payments, and document verification while improving accessibility to certified instructors.

Objective	To develop a secure, user-friendly web and mobile system that enables instructor registration, student sign-up, lesson booking, payment integration (Future phase), and rating/review features.
Corporate Goals Addressed	• Promote road-safety education through accessible technology. • Support independent instructors with digital visibility and income growth. • Offer students verified, affordable, and convenient driving-lesson options.
Planned Start Date	Sept 15, 2025
Planned End Date	March 27, 2026

2. Project Approvers, Reviews and Distribution List

Approvers, reviewers and distribution list

Project Role	Name	E-mail	Date
Team Lead	Heemal Syangbo	Heemal.Syangbo@georgebrown.ca	2025-10-06
Team Member	Anudhin Thomas	Anudhin.thomas@georgebrown.ca	2025-10-06
Team Member	Jeffin Yohannan	Jeffin.Yohannan@georgebrown.ca	2025-10-06
Team Member	Nasharudhin Feroz	Nasharudhin.Feroz@georgebrown.ca	2025-10-06

3. Scope

Define the sum total of all of its products and their requirements or features.

In Scope	Out of Scope
Student and Instructor authentication (JWT-based).	Third-party payment gateway integration in Sprint 2.
Instructor verification flow (admin approval).	Real-time map navigation or chat features.
Profile management and document upload.	
Lesson booking, rescheduling, and cancellation.	
Review and rating system.	
Notifications and email confirmations.	

4. Deliverables

This project will deliver the following.

Deliverable	Description
Functional Prototype	Fully working web application covering auth, profiles, booking system and admin panel.
Database & API	MongoDB database with Express REST API supporting CRUD operations and JWT security.
Sprint 2 Documentation	Completed Project Plan, Team Charter, and updated technical docs.

5. Assumptions

This project makes the following assumptions;

- All team members share equal responsibility for development and testing.
- Cloud deployment may use Render or Firebase for testing purposes.
- User data stored securely in MongoDB Atlas with basic access control.
- Instructor verification handled through manual admin review in MVP.

6. Dependencies

The following are the internal and external dependencies that will have to be acknowledged and addressed;

- Node.js and MongoDB environment set up.
- GitHub repository and branch coordination.

7. Risk Management

Potential Risk	Severity (H/M/L)	Likelihood (H/M/L)	Management Strategy
Merge conflicts or version issues	M	M	Use Git branching standards and pull request reviews.
Backend API failure	H	M	Add unit tests and Postman validation per endpoint.
Time constraints	H	H	Weekly milestone tracking and division of tasks.
Deployment errors	M	M	Test locally before pushing to cloud.
Incomplete data validation	L	M	Implement server-side and client-side validation.

8. Communication

Reporting

The following reports will be produced;

Report	Audience	Frequency
Sprint Status Report	Team T06	Weekly
Progress Update in Teams	Team T06	Twice per week
GitHub Commits & PR Logs	Team T06	Continuous

Meetings

The following meetings/communication will be established;

Meeting	Purpose	Attendees	Frequency
Sprint Planning	Define upcoming tasks and responsibilities.	All members	Weekly
Code Review	Discuss technical issues and testing results.	All members	Twice per week
Team Review	Check progress and take team member feedbacks.	All members	Bi-weekly


9. Task Listing (WBS- Work Breakdown Structure)

The following resource proposal template summarizes the resource hours committed to this project, upon final approval of this document.

Reference	Tasks	Duration	Dependency
A	Backend setup (Node.js, Express, MongoDB)	1 week	None
B	Authentication (JWT, roles)	1 week	A
C	Instructor profile + verification module	1 week	B
D	Booking system (UI + API)	1 week	C
E	Reviews + notifications	1 week	D
F	Testing & bug fixing	2 weeks	A-E
G	Documentation + video demo	1 week	F

10. Gantt Chart

Have also attached as separate file.

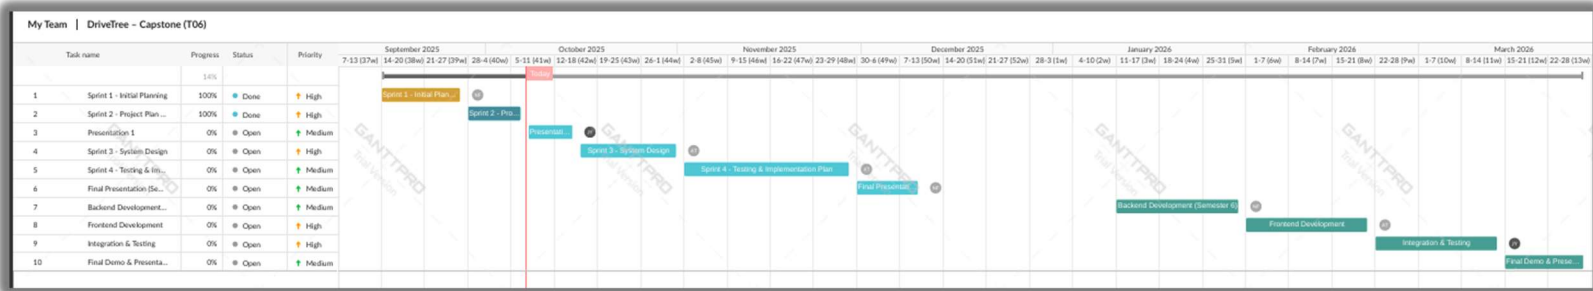

11. Milestones

Major Activity or Milestone	Estimated Milestone Target date	Owner/Reviewer Team Members
Sprint 2 Document Submission (Project Plan + Team Charter)	October 7, 2025	Full Team – T06
Sprint 2 Presentation	October 15, 2025	Full Team – T06
System Design Completion (Sprint 3)	October 31, 2025	Full Team – T06
Implementation Plan & Testing Strategy (Sprint 4)	November 30, 2025	Full Team – T06
Final Presentation – Semester 5	December 10, 2025	Full Team – T06
Backend Development Completion	January 31, 2026	Full Team – T06
Frontend Development Completion	February 20, 2026	Full Team – T06
Integration & Testing Completed	March 15, 2026	Full Team – T06
Final Demo & Presentation	March 27, 2026	Full Team – T06

12. RAM – Responsibility Assignment Matrix

Create a RAM from your Task Listing. A sample is shown below:

Project Team Responsibilities				
Project Name:		DriveTree		
Task	Heemal Syangbo	Anudhin Thomas	Jeffin Yohannan	Nasharudhin Feroz
Sprint 1 – Initial Planning	P	S	S	S
Sprint 2 – Project Plan & Team Charter	S	P	S	S
Presentation 1 (Sprint 2)	S	S	S	P
Sprint 3 – System Design		S		P
Sprint 4 – Testing & Implementation Plan	P		S	
Final Presentation (Semester 5)	P	S	S	S
Backend Development	P			S
Frontend Development		P	S	
Integration & Testing	P	S		
Final Demo & Presentation	P	S	S	S

13. Approval

The signatures below indicate their approval of the contents of this document.

Project Role	Name	Signature	Date
Team Lead	Heemal Syangbo	H.S	2025-10-06
Team Member	Anudhin Thomas	A.T	2025-10-06
Team Member	Jeffin Yohannan	J.Y	2025-10-06
Team Member	Nasharudhin Feroz	N.F	2025-10-06
